
Annex A - Part 1: Common safety lapses from WAH inspections





Unsafe scaffolds- work platform deckings are not secured and flushed on scaffolds.

There are also no guard rails and toe-boards installed according to requirements under the WSH (Scaffolds) Regulations.

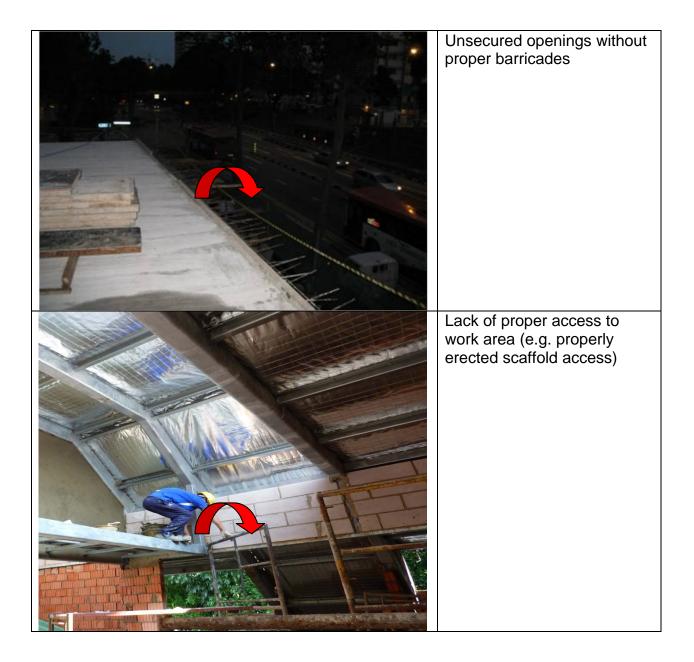

Failure to provide adequate anchorage for use of fall protection equipment- worker is wearing safety harness, however, there is no anchorage points (e.g. lifelines) provided by the contractor for him to secure his safety harness.



Poor housekeeping resulting in tripping hazards



Lack of control measures for work on fragile roof surface (e.g. roof skylight of existing factory premises)
