








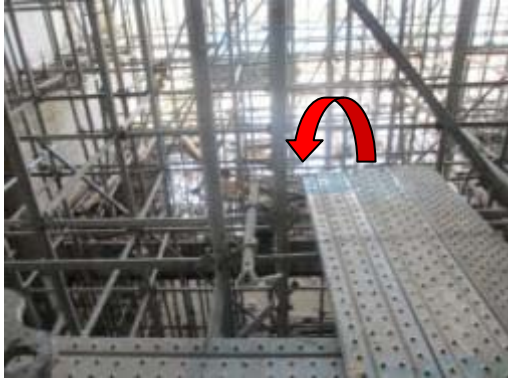

Photographs of WAH Violations

S/No	Photo	Description
1		<ul style="list-style-type: none"> The occupier at this worksite failed to implement adequate fall prevention measures, at this extended work platform. Workers at the site faced the risk of falling 2 metres into a void area.
2		<ul style="list-style-type: none"> The occupier at this worksite failed to implement adequate fall prevention measures, at this extended work platform. Workers at the site faced the risk of falling 2 metres into a void area.
3		<ul style="list-style-type: none"> The occupier at this worksite failed to implement fall prevention measures at an open side of the 33rd storey of a building under construction. An inspection of the worksite showed that the entire level had housekeeping problems that posed trip hazards to workers.

4		<ul style="list-style-type: none">• The occupier at this worksite failed to implement fall prevention measures at an opening. Workers at the site faced the risk of falling more than 2 metres through the opening.
5		<ul style="list-style-type: none">• The occupier at this worksite failed to implement fall prevention measures at this roof of a car porch r under construction.
6		<ul style="list-style-type: none">• The occupier at this worksite failed to implement fall prevention measures along the multiple open sides at this work area. Workers at the site faced the risk of falling more than 2 metres through the open sides.

7		<ul style="list-style-type: none">• The occupier at this worksite provided poor guardrails that were not properly maintained. The guardrails did not serve its purpose of fall prevention.
8		<ul style="list-style-type: none">• The occupier at this worksite had allowed wooden planks to be used to cover an opening which could lead to a 2 metre fall, but the wooden planks were not properly secured. Thus, they could be accidentally moved.
9		<ul style="list-style-type: none">• The occupier at this worksite did not properly cover this opening, through which a worker could fall more than 2 metres.
